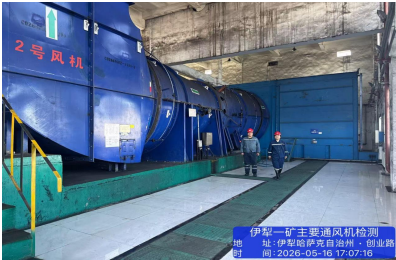


序号	报告编号	发布日期	结论	影像资料
2	GX-B1425/23-8-26001	2026年6月9日	1. 主通风机正常通风风量：南风井主通风机105.84 m ³ /s，北风井主通风机214.44 m ³ /s； 2. 主通风机反风量：南风井主通风机75.26 m ³ /s，北风井主通风机160.38 m ³ /s； 3. 主通风机反风率：南风井主通风机71.11%，北风井主通风机74.79%； 4. 矿井风流反向用时：7分30秒。	
3	GX-B1340/26-8-26021	2026. 6. 15	合格	

4	GX-B1340/26-8-26022	2026. 6. 15	合格	
5	GX-B1340/25-8-26019	2026. 6. 15	合格。	

6	GX-B1340/25-8-26020	2026. 6. 15	合格。	
7	GX-B1341/24-8-26020	2026. 6. 12	综合判定：合格	

8	GX-B1343/26-8-26015	2026. 6. 12	1. 矿井实测风量： 32.99 m³/s; 2. 通风机负压：- 265m中段主通风机 2100Pa; 3. 矿井通风阻力： 2080.0 Pa。	 
9	GX-B1347/26-8-26014	2026. 6. 12	综合指标：86.8%， 合格	 
